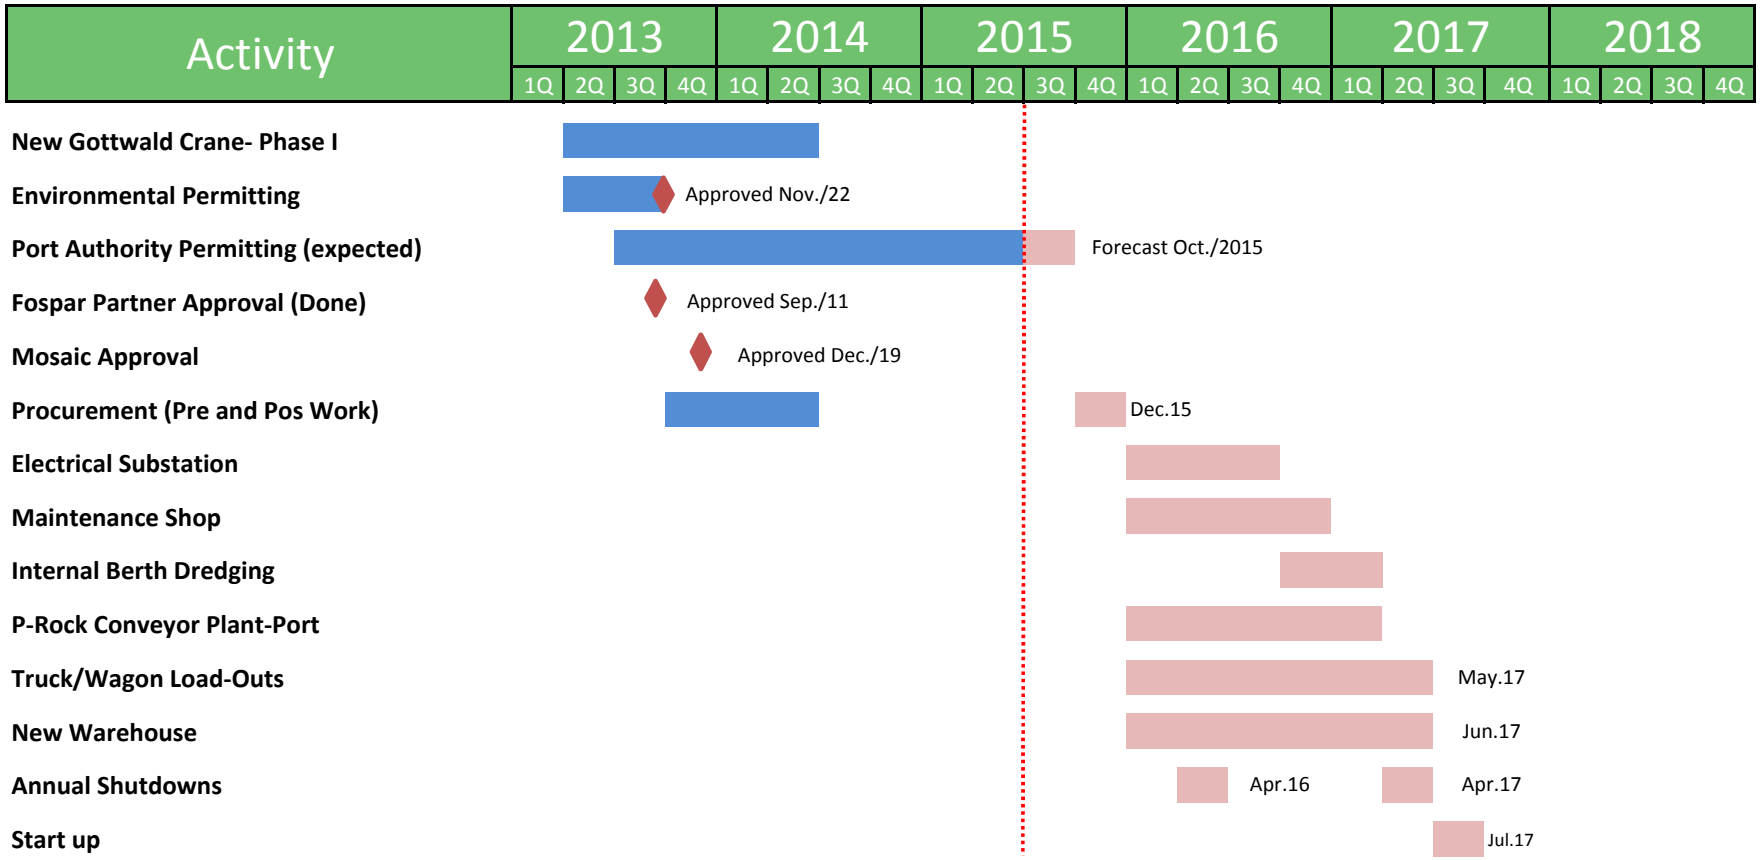
Activity
2013
2014
2015
2016
2017
2018
1Q 2Q 3Q 4Q 1Q 2Q 3Q 4Q 1Q 2Q 3Q 4Q 1Q 2Q 3Q 4Q 1Q 2Q 3Q 4Q 1Q 2Q 3Q 4Q
New Gottwald Crane- Phase I
Environmental Permitting
Approved Nov./22
Port Authority Permitting (expected)
Forecast Oct./2015
Fospar Partner Approval (Done)
Approved Sep./11
Mosaic Approval
Approved Dec./19
Procurement (Pre and Pos Work)
Dec.15
Electrical Substation
Maintenance Shop
Internal Berth Dredging
P-Rock Conveyor Plant-Port
Truck/Wagon Load-Outs
May.17
New Warehouse
Jun.17
Annual Shutdowns
Apr.16
Apr.17
Start up
Jul.17
